



Dart Aerospace Ltd.
1270 Aberdeen St
Hawkesbury, ON
K6A 1K7
Canada

Tel (613) 632-5200
Fax 613 632-5246

D119-796-141
Job Sheet 187277



Part No: D119-796-141

Job Qty: 1 ea

Part Name: Fwd Crosstube Installation Without Step (No Hardware)



Part Weight: 0 lbs

Status: New

Priority: Medium

Job Created: 11/29/18

Job Tracking No:

Due Date: 1/4/19

Created By: Jesse White

Type: SOLD

Description:

Note: DRWG D119-795-141 REV:H IPP REV:C 14.11.19 AS PER REV:C DD VERF:JLM IPP REV:D 14.12.12 AS PER REV:pd1 DD VERF:JLM IPP REV:E 15.02.11 AS PER REV F JLM VERIFIED BY:DD

Ship Via:

Bill of Materials

Job Routing

Op No	Operation	Qty	Start Date	Due Date	Standard		Workcenter/Supplier		Sign-off
					Setup Hrs	Run Hrs	Workcenter / Supplier	Lead Time	
90	Start up Operation	1 Ea	1/4/19	1/4/19	0.00	0.00	Start Up Crosstubes-1		DB 12/10/2018
130	CNC Bend Crosstubes	1 pcs	1/4/19	1/4/19	0.00	3.85	CNC Bend Crosstube		DP2 / DB 12/10/2018
140	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC15		
145	Crosstubes	1 pcs	1/4/19	1/4/19	0.00	3.06	Crosstubes-1		GP 18-12-12
150	Crosstubes	1 pcs	1/4/19	1/4/19	0.00	3.06	Crosstubes-1		GP 18-12-12
160	HandFXtube	1 pcs	1/4/19	1/4/19	0.00	1.49	HandFinish5		GP 18-12-12
175	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC7-1		
180	Outsource	1 pcs	1/4/19	1/4/19			SKY002-VC	2	CT 18-12-12
190	Packaging	1 pcs	1/4/19	1/4/19	0.00	0.00	Packaging1-1		DEC 17 2018
200	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC5		
230	SprayPaint	1 pcs	1/4/19	1/4/19	0.00	1.36	Spray Paint		AB 18-12-29
240	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC14		
242	Crosstubes	1 pcs	1/4/19	1/4/19	0.00	3.06	Crosstubes-1		AR 19-1-12
244	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC5		
246	SprayPaint	1 pcs	1/4/19	1/4/19	0.00	1.36	Spray Paint		AB 19-1-22
248	SprayPaint	1 pcs	1/4/19	1/4/19	0.00	1.36	Spray Paint		AR 19-1-23
250	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC14		
252	Crosstubes	1 pcs	1/4/19	1/4/19	0.00	3.06	Crosstubes-1		AR 19-1-23
260	QC	1 pcs	1/4/19	1/4/19	0.00	0.00	QC5		
275	DC	1 pcs	1/4/19	1/4/19	0.00	0.00	DC		NR
290	Packaging	1 pcs	1/4/19	1/4/19	0.00	0.00	Packaging3-1		AR 19-1-23
300	QC21-FG	1 Ea	1/4/19	1/4/19	0.00	0.00	QC21		DAS 21 JAN 23 2019

Part Op 130 - Bend tube as per Dwg D119-796-141 using CNC bender program

Descriptions: 145 - 1- CUT TUBE AT HEIGHT ON FAI SHEET 2- VERIFY HEIGHT: _____ BY QC15 LEVEL _____

INSPECTOR: _____ 3- DEBURR CUT SURFACE

150 - ***** ENSURE PROPER JIG POSITIONING ***** ENSURE PROPER JIG POSITIONING

***** 1-DRILL TUBE AS PER DWG USING DT _____ 2- DRILL RIVET HOLES USING DT8787 FWD 3- DEBURR AND C'SINK RIVET HOLES AS PER DWG 4- FLIP TUBE, REPEAT STEP 2 AND 3 5- SCRIBE PART# AND BATCH# USING VIBRATING STYLUS ON INSIDE OF CUFF AS PER DWG D119-796-141 6- INSPECT AND REMOVE ALL MARKS FROM TUBE WITHIN LIMITS ON DWG D119-796-141

160 - ***IMMEDIATELY AFTER GRINDING*** 1- handfinish X-TUBE INSIDE AND OUT 2- ALODINE AND ACID ETCH X-TUBE INSIDE AND OUT AS PER QSI005.

Entered: _____ Date: _____



WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042) _____	
Description Work Order Deviation		Disposition		Completed By	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Presservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐ ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details: _____					

180 - *** WEAR LATEX GLOVES WHEN HANDLING CROSSTUBE*** Liquid Penetrant Inspection as per QSI 038Or Issue P/O: _____ LPI as per ASTM 1417 Level 2 Attach copy of NDT results to work order

190 - Ensure copy of NDT results attached to work order.

200 - *** WEAR LATEX GLOVES WHEN HANDLING CROSSTUBE*** Inspect for damage & ensure results are as per Dwg D119-796-141

230 - ***VERIFY BY _____ BATCH # TO MATCH W/O _____ ***VERIFY BY _____ PART # TO MATCH W/O _____ ***MASK SCRIBE B# & P# AND VERIFY*** 1- Prime Inside of tube. 2- Install nut plates as per dwg (D2873-043) 3- Mask cuffs per note#2. 4- Prime exterior of tube per QSI005. Primer Batch: 138962 Start Time: 19-1-19 Finish Time: 19-1-22

240 - ***VERIFY BY _____ BATCH # TO MATCH W/O _____

242 - Assemble as per dwg D119-796-141 and Qsi 015 1- Abrade mating surfaces with Scotch Brite 7447 and clean with Dupont 4105s or equivalent as per dwg. 2- Install D5152-041 with proseal 890 on concave surface, 0.100" MIN thick as per dwg using DT10089 (identified right and left) ****MAINTAIN CLAMPING PRESSURE ON FOR MIN 72HRS***** Proseal Batch: 138976 EXP: 6/19 PROSEAL CURE TIME 72 HOURS: Start: 19-1-19 Finish: 19-1-22 3- Install support and shim using proseal 890 per dwg and clamp in position.

244 - ***VERIFY BY _____ BATCH # TO MATCH W/O _____

246 - ***VERIFY BY _____ BATCH # TO MATCH W/O _____ 1- Remove all non-fixed hardware and clean any excess proseal. 2- Scuff tube with Scotch Brite 7447. 3- Mask cuff per note#2. 4- Prime as per dwg and QSI005 5- Apply matte clear as per dwg and QSI005 Clear Batch: 138875 Primer 5143305

248 - ***VERIFY BY _____ BATCH # TO MATCH W/O _____ 1- Mask underside of tube as per dwg. Mask cuff per note#2. 2- Scuff tube with Scotch Brite 7447 3- Paint outside of crosstube Paint Batch: 5140325

250 - ***VERIFY BY _____ BATCH # TO MATCH W/O _____

252 - 1- Re-install non fixed hardware per dwg ***Torque all clamps to 80-100 IN-LBS.*** 2- Apply a filet-seal of proseal 890 around supports. Allow proseal to dry before inspecting. Proseal 890 Batch: _____ EXP: _____ PROSEAL CURE TIME 72 HOURS: Start: _____ Finish: _____

260 - ***RE-CHECK TORCQUE ON CLAMP AFTER PROSEAL HAS CURED AS PER DWG.*** **VERIFY BY _____ BATCH # TO MATCH W/O _____

275 - Photocopy bluefile and create labels as per PPP D119-796-141 chg 004

290 - Identify and pack for shipping as per PPP D119-796-141
on w/o 187556

Job BOM

Part / Item	Component Name	Quantity	Operation	Container
D119-796-141TRN	Crosstube Turning Detail	1 Ea (1 ea)	90-Start up Operation	<u>5126774</u>
CR3212-4-08	Rivet	16 Ea (16 ea)	242-Crosstubes	
D2873-043	Nut Plate Assembly	4 Ea (4 ea)	242-Crosstubes	
D5123-3	Clamp Cushion	4 Ea (4 ea)	242-Crosstubes	
D5124-1	Fwd Support	2 Ea (2 ea)	242-Crosstubes	
D5152-041	Fwd Post Mount Assembly	2 Ea (2 ea)	242-Crosstubes	
D5305-1	Shim	2 Ea (2 ea)	242-Crosstubes	
MS21920-24	Clamp	4 Ea (4 ea)	242-Crosstubes	

Job Allocations

Operation	Component Part	Required	Inventory	Allocated
90-Start up Operation	D119-796-141TRN	1	5	0
242-Crosstubes	CR3212-4-08 <u>5058457</u>	<u>16</u>	169	0
	D2873-043 <u>5090584</u>	<u>4</u>	25	0
	D5123-3 <u>5079324</u>	<u>4</u>	253	0
	D5124-1 <u>5091939</u>	<u>2</u>	12	0
	D5152-041 <u>5089481</u>	<u>2</u>	6	0
	D5305-1 <u>5091791</u>	<u>2</u>	13	0
	MS21920-24 <u>5065334</u>	<u>4</u>	56	0



Container No: S136226



Part: D119-796-141

Job No: 187277

Serial No/Batch: S136226

Revision: F,H

Inspector:

Exp Date:

Instructions: TC STC SH14-45-Issue 1, FAA STC SR03504NY 15/01/28, EASA

Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K64 1K7
CANADA
TEL.: 1 613 632-5200
Email: sales@dartaero.com
www.dartaerospace.com

Plex 11/29/18 12:58 PM dart.white.jesse

Entered: _____ Date: _____



WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date :	Sequence #:	QTY Affected :		MRB (QSI042)	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor		
			QC / QA Coordinator		
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Preservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details: _____					

Part Specifications					
Spec No	Description	Target/Tolerance	Limits	Type	Special Comments
1	Crosstube Assembly (AW119 MKI Fwd)	6.000Inches $\pm$ 0.030	6.030 5.970		
2	Crosstube Assembly (AW119 MKI Fwd)	2.516Inches $\pm$ 0.005	2.521 2.511		
3	Crosstube Assembly (AW119 MKI Fwd)	2.333Inches + 0.005 - 0.000	2.338 2.333		
4	Crosstube Assembly (AW119 MKI Fwd)	2.333Inches + 0.005 - 0.000	2.338 2.333		
5	Crosstube Assembly (AW119 MKI Fwd)	2.408Inches + 0.005 - 0.000	2.413 2.408		
6	Crosstube Assembly (AW119 MKI Fwd)	2.502Inches + 0.005 - 0.000	2.507 2.502		
7	Crosstube Assembly (AW119 MKI Fwd)	2.596Inches + 0.005 - 0.000	2.601 2.596		
8	Crosstube Assembly (AW119 MKI Fwd)	2.596Inches + 0.005 - 0.000	2.601 2.596		
9	Crosstube Assembly (AW119 MKI Fwd)	6.000Inches $\pm$ 0.030	6.030 5.970		
10	Crosstube Assembly (AW119 MKI Fwd)	2.516Inches $\pm$ 0.005	2.521 2.511		
11	Crosstube Assembly (AW119 MKI Fwd)	2.333Inches + 0.005 - 0.000	2.338 2.333		
12	Crosstube Assembly (AW119 MKI Fwd)	2.333Inches + 0.005 - 0.000	2.338 2.333		
13	Crosstube Assembly (AW119 MKI Fwd)	2.408Inches + 0.005 - 0.000	2.413 2.408		
14	Crosstube Assembly (AW119 MKI Fwd)	2.502Inches + 0.005 - 0.000	2.507 2.502		
15	Crosstube Assembly (AW119 MKI Fwd)	2.596Inches + 0.005 - 0.000	2.601 2.596		
16	Crosstube Assembly (AW119 MKI Fwd)	2.596Inches + 0.005 - 0.000	2.601 2.596		
17	Crosstube Assembly (AW119 MKI Fwd)	102.260Inches $\pm$ 0.020	102.280 102.240		

Plex 11/29/18 12:58 PM dart.white.jesse

Entered: _____ Date: _____



WORK ORDER NON-CONFORMANCE / ROUTE UPDATE


NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date :	Sequence #:	QTY Affected :		MRB (QSI042)	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Preservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

DART AEROSPACE LTD		Work Order:	
Description: Crosstube Fwd, with Step		Part Number:	D119-796-141
Inspection Dwg: D119-796-141 Rev: H			Page 1 of 1

Required Dimension	Min	Max
Height	21.490	21.750
1/2 Span	39.820	40.080
Angle	54°	57°
Total Span	79.640	80.160
Bending Passes	8	--
Crushing	--	6.8%

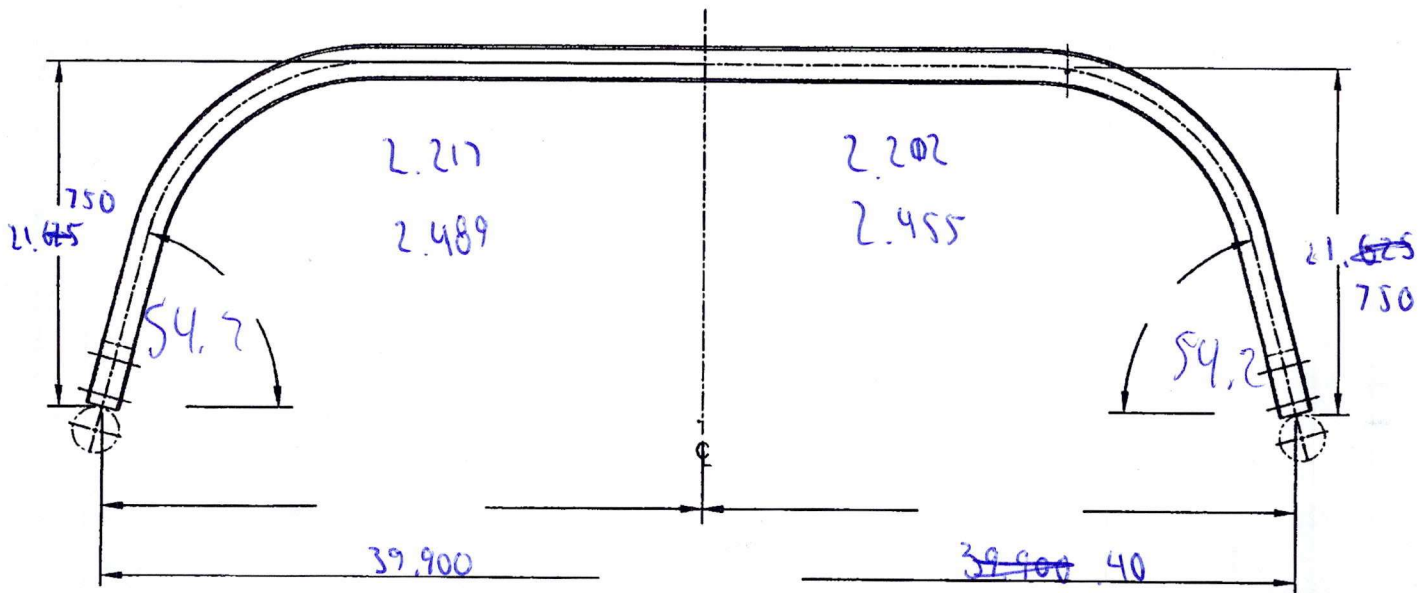

	12 Side A	12 Side B
Bending Passes	5.8%	5.7%
Crushing		
Comments		

QC15 Inspection	13-12-11
Date	

Rev	Date	Change	Revised by	Approved
A	15.04.14	New Issue	KJ	
B	15.11.12	Dwg Rev updated	KJ	
C	16.01.15	Dwg Rev updated	KJ	47

Entered: _____ Date: _____




WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042)	
Description Work Order Deviation		Disposition		Completed By	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Preservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐ ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

ITEM	QTY	P/N	DESCRIPTION
	X	D119-796-141	XTUBE ASSY (AW119 MKII FWD)
1	1	D119-796-141BND	CROSSTUBE, FWD
2	4	D2873-043	RADIUS BLOCK
3	4	D5123-3	CLAMP CUSHION
4	2	D5124-1	FWD SUPPORT
5	2	D5152-041	FWD POST MOUNT ASSY
6	2	D5305-1	SHIM
7	16	CR3212-4-08	RIVET, BLIND CSK
8	4	MS21920-24	CLAMP

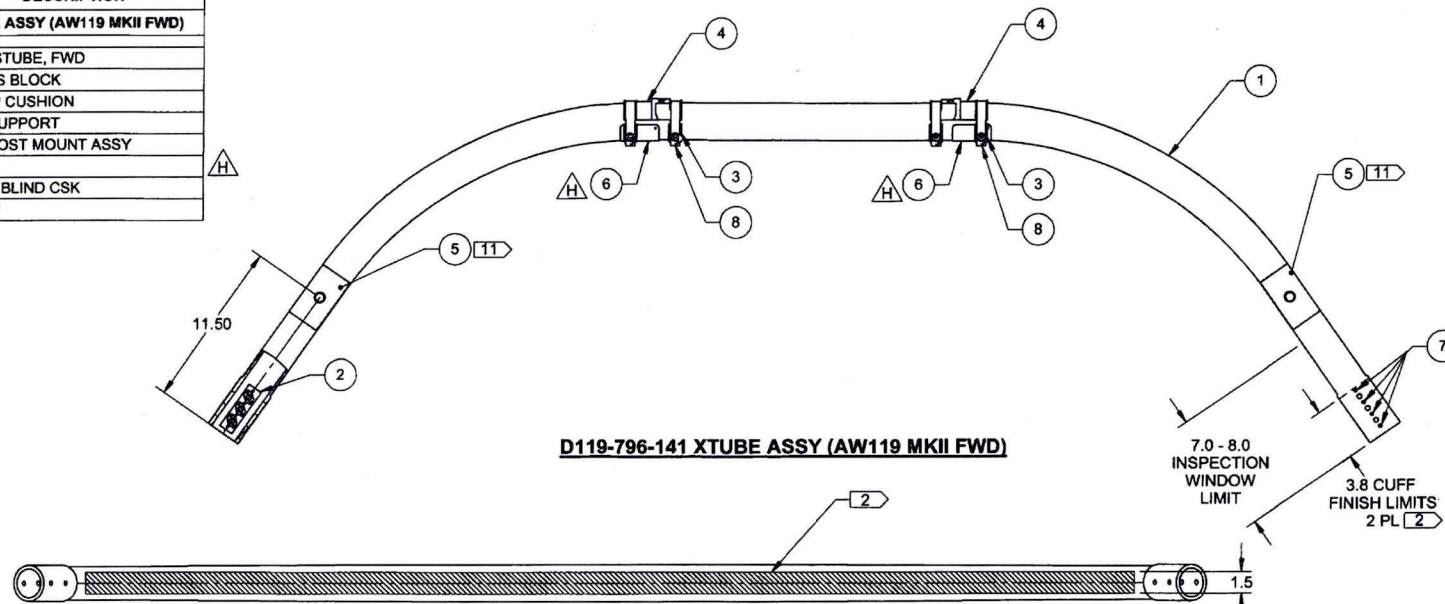

RELEASED
2015-11-04
ECN 15-642

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: APPLY MATTE CLEAR COAT PER QSI 005 4.2
MASK D5124-1 FWD SUPPORTS, D5305-1 SHIMS AS WELL AS UNDERSIDE OF CROSSTUBE AS SHOWN (B3-1, HATCHED AREA),
PAINT OUTSIDE PER DART QSI 005 4.2 AFTER APPLYING CLEAR COAT
DO NOT APPLY FINISH (PAINT OR CLEAR COAT) TO CUFFS IN LOCATION SHOWN, MASK PRIOR TO FINISHING
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY USING PART NUMBER "D119-796-141" AND BATCH NUMBER ON INSIDE OF CUFF PER QSI 044 6.4
- 7) WEIGHT: 18.54 lbs
- 8) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE.
THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM DEFECTS SUCH AS SCRATCHES, NICKS OR DENTS.
DEFECTS UP TO 0.005 MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.
- 9) PRIOR TO FINISHING, ABRASE MATING SURFACES OF D5124-1 FWD SUPPORTS AND CROSSTUBE WITH SCOTCH BRITE 7447 RED AND REMOVE RESIDUE WITH DUPONT 4105S WASH'N'WIPE DEGREASER. APPLY A 0.1 MIN THK LAYER OF PROSEAL 890 ON THE INSIDE CONCAVE SURFACE OF THE D5124-1 FWD SUPPORTS AND INSTALL AT AN 8.4" OFFSET FROM THE CROSSTUBE BENDING PLANE. INSTALL THE MS21920-24 CLAMPS AND D5123-3 CLAMP CUSHIONS WHILE WET.
- 10) TORQUE MS21920 CLAMPS 80 - 100 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY, THE NUT IS FACING AFT AND HAS NOT BOTTOMED-OUT AFTER TORQUING. PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.
- 11) PRIOR TO FINISHING, ABRASE MATING SURFACES OF CROSSTUBE AND D5152-041 WITH SCOTCH BRITE 7447 RED AND REMOVE RESIDUE WITH DUPONT 4105S WASH'N'WIPE DEGREASER. INSTALL D5152-041 WITH LAYER OF PROSEAL 890 ON INSIDE CONCAVE SURFACE, 0.1 MIN THK. LOCATE D5152-041 USING TOOL DT10089.
- 12) PRIOR TO FINISHING, ABRASE MATING SURFACES OF CROSSTUBE AND D5305-1 SHIM WITH SCOTCH BRITE 7447 RED AND REMOVE RESIDUE WITH DUPONT 4105S WASH'N'WIPE DEGREASER. INSTALL D5305-1 SHIM WITH LAYER OF PROSEAL 890 ON INSIDE CONCAVE SURFACE, 0.1 MIN THK. USE ADDITIONAL TEMPORARY MS21920-24 CLAMP TO APPLY CLAMPING PRESSURE FOR 72 HOURS.

H	ADD D5305-1 SHIM, D6024-103 WAS D6005-103, D5124-1 NOW INSTALLED ON PRIMER	AP	15.10.13
G	FINISHING ORDER ADJUSTED, CR3212-4-08 WAS -07, CUFF DIA TOLERANCE INCREASED TO +/- 0.005	AP	15.04.24
F	REMOVED PRIME/ PAINT ON CUFFS. 2.516 WAS 2.500 (C8-5)	AP	15.02.03
E	D5152-041 FWD STEP POST ASSY WAS D5150-1 STEP POST, SCOTCH BRITE 7447 RED WAS 180 GRIT SANDPAPER, ANGLE (B7-2) DIMENSIONED FROM NEW DATUM	DB	15.01.15
D	ADD D5150-1 STEP POST (2X), MOVED INSPECTION WINDOW DETAIL TO SHEET 1, MODIFIED NOTES ON SHT 1 & 3	DB	14.11.25
C	CR3212-4-07 RIVETS WERE CR3212-4-09, 7.5 DEG CUFF ANGLE OFFSET REMOVED (SHT 3), CUFF DIAMETER ON D119-796-141TRN REDUCED TO 2.500, ADDED INSPECTION WINDOW (B7-3), ADDED SHT 4	AP	14.10.23
B	ADDED D2873-043 RADIUS BLOCK, CR3212-4-09 RIVETS, ADDED SKIDTUBE REFERENCE FOR LOCATING CUFF HOLES, RE-ORGANIZED NOTES AND REMOVED REDUNDANT INFORMATION	AP	14.09.02
A	NEW ISSUE	AP	14.08.09
REV.	DESCRIPTION	BY	DATE
DESIGN	AP		
DRAWN	AP		
CHECKED	AJS		
MFG. APPR.	JLM		
APPROVED	WM		
DE APPR.	DS		
DATE	15.10.13		

DART AEROSPACE LTD
HAWKESBURY, ONTARIO, CANADA

DRAWING NO. **D119-796-141** REV. H
SHEET 1 OF 6

TITLE **XTUBE ASSY (AW119 MKII FWD)** SCALE NTS

COPYRIGHT © 2014 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION OF DART AEROSPACE LTD.

Entered: _____ Date: _____




WORK ORDER NON-CONFORMANCE / ROUTE UPDATE


NCR No. _____

Route update only ☐


Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date :	Sequence #:	QTY Affected :		MRB (QSI042)	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Presservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

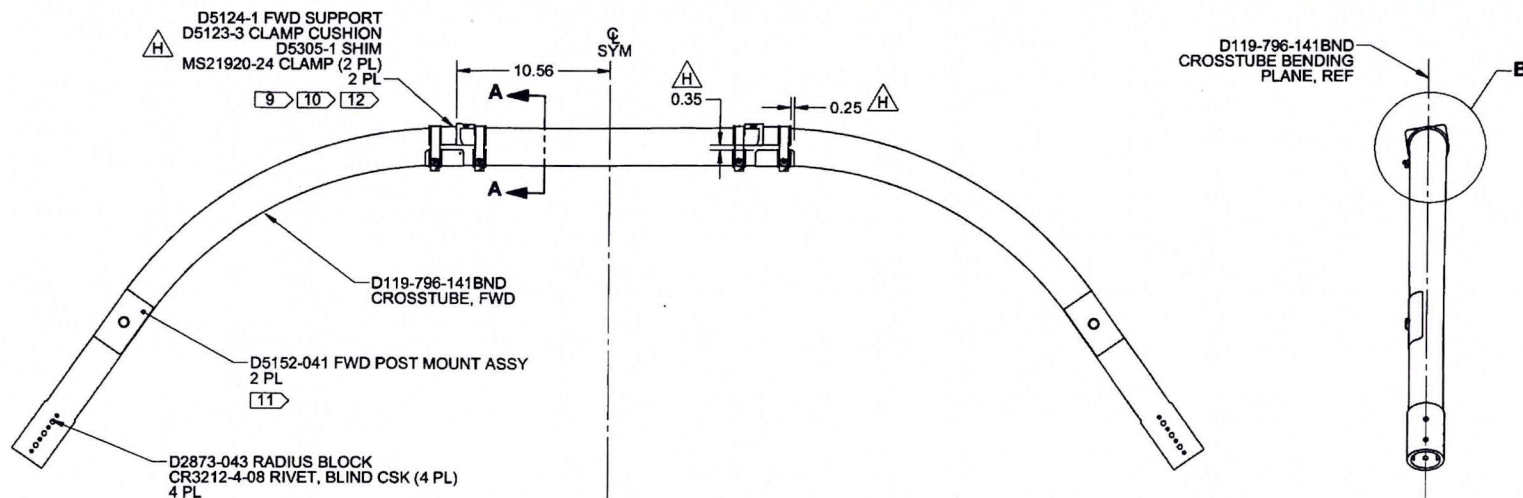

D119-796-141 XTUBE ASSY (AW119 MKII FWD)

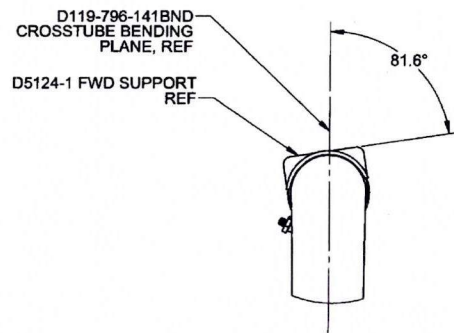

DETAIL B
SCALE 2X



SECTION A-A
SCALE 2X

RELEASED
2015-11-04

APPROVED

DESIGN	AP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	AJS	DRAWING NO.	REV. H
MFG. APPR.	JLM	D119-796-141	SHEET 2 OF 6
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII FWD)	NTS
DATE	15.10.13	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

Entered: _____ Date: _____




WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042)	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Presservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

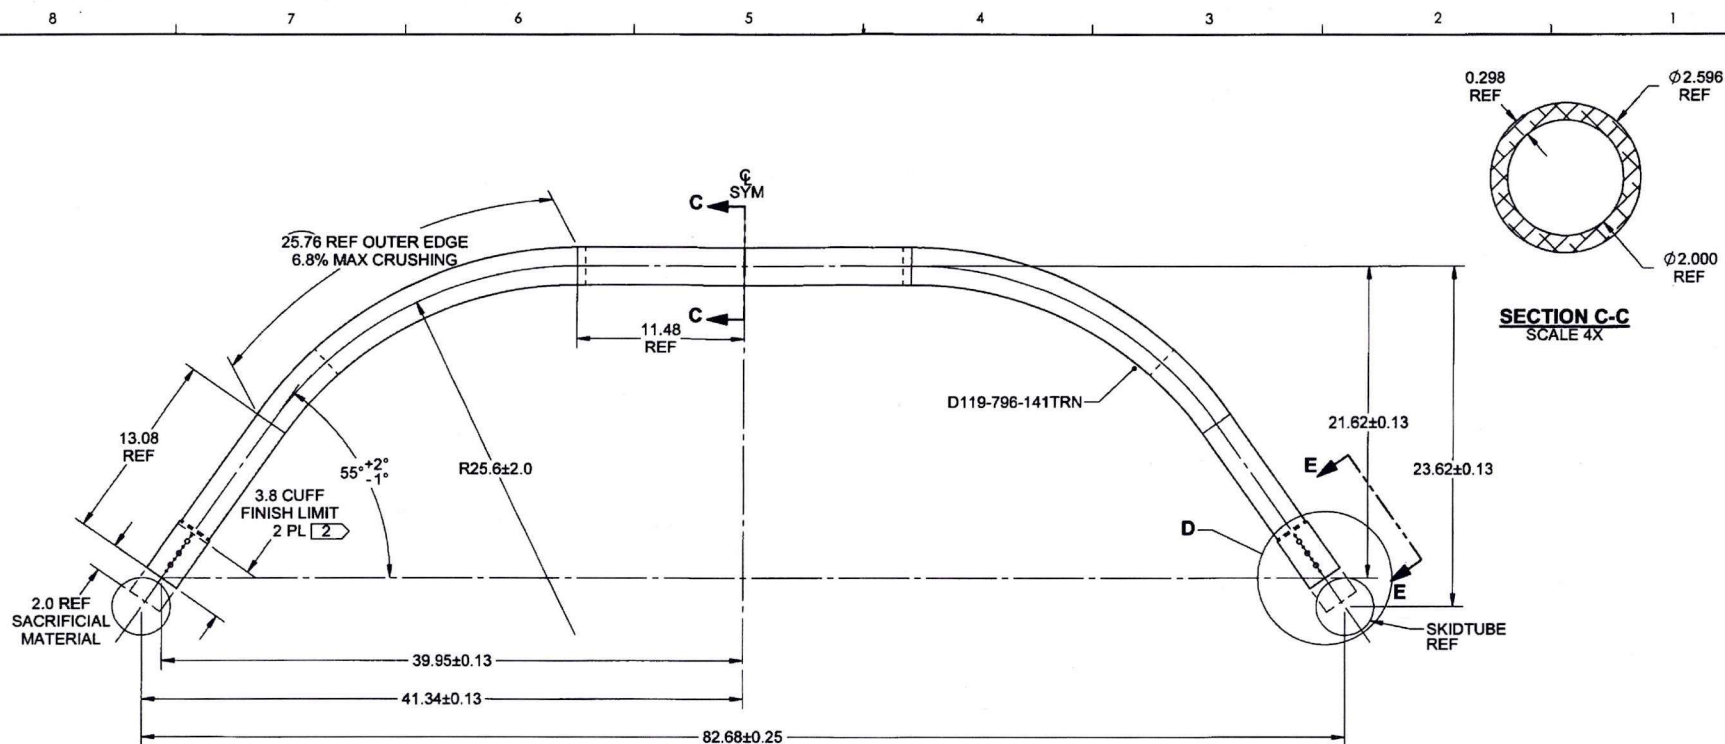

D119-796-141BND CROSSTUBE, FWD 9
BENDING AND DRILLING DETAIL

NOTES:

- 1) MATERIAL: MADE FROM D119-796-141TRN
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
DO NOT APPLY PRIMER TO CUFFS IN LOCATION SHOWN, MASK PRIOR TO FINISHING
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 16.70 lbs
- 8) PART IS SYMMETRICAL ABOUT CENTERLINE
- 9) BEND PROGRESSIVELY WITH A MINIMUM OF 8 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6.8% BASED ON OD.
- 10) LIQUID PENETRANT INSPECT OUTSIDE SURFACE OF CROSSTUBE PER QSI 038
- 11) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM DEFECTS SUCH AS SCRATCHES, NICKS OR DENTS. DEFECTS UP TO 0.005 MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.

RELEASED
2015-11-04

APPROVED

DESIGN	AP	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	AJS	DRAWING NO.	REV. H
MFG. APPR.	JLM	D119-796-141	SHEET 3 OF 8
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII FWD)	NTS
DATE	15.10.13	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

Entered: _____ Date: _____




WORK ORDER NON-CONFORMANCE / ROUTE UPDATE


NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042)	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Presservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

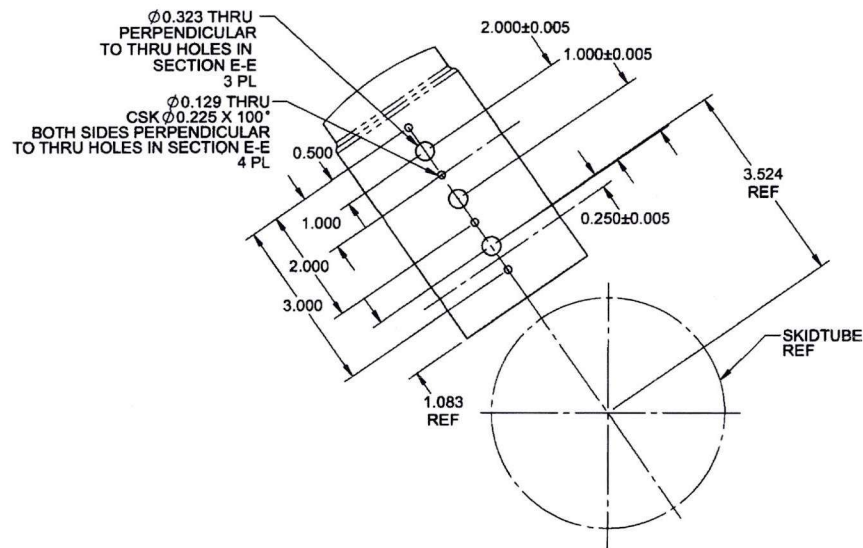

VIEW D
SCALE 4X

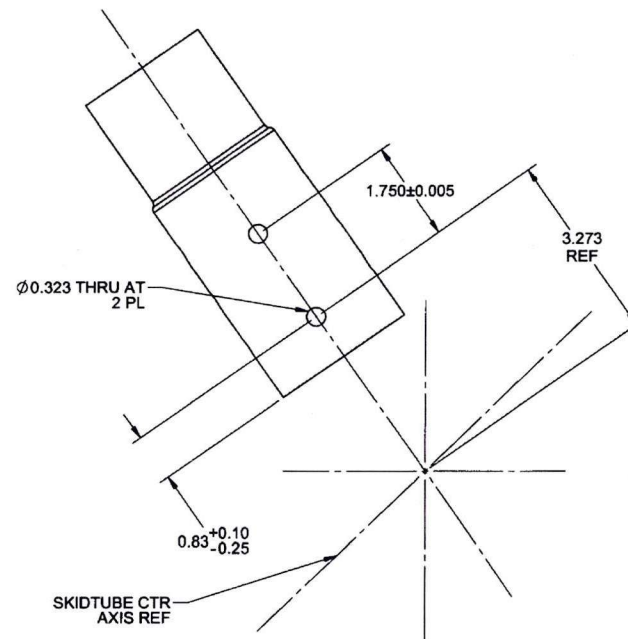

VIEW E-E
SCALE 2X

RELEASED
2015-11-04

APPROVED

DESIGN	AP	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	AJS	DRAWING NO.	REV. H
MFG. APPR.	JLM	D119-796-141	SHEET 4 OF 6
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII FWD)	NTS
DATE	15.10.13	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

Entered: _____ Date: _____




WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042)	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Preservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

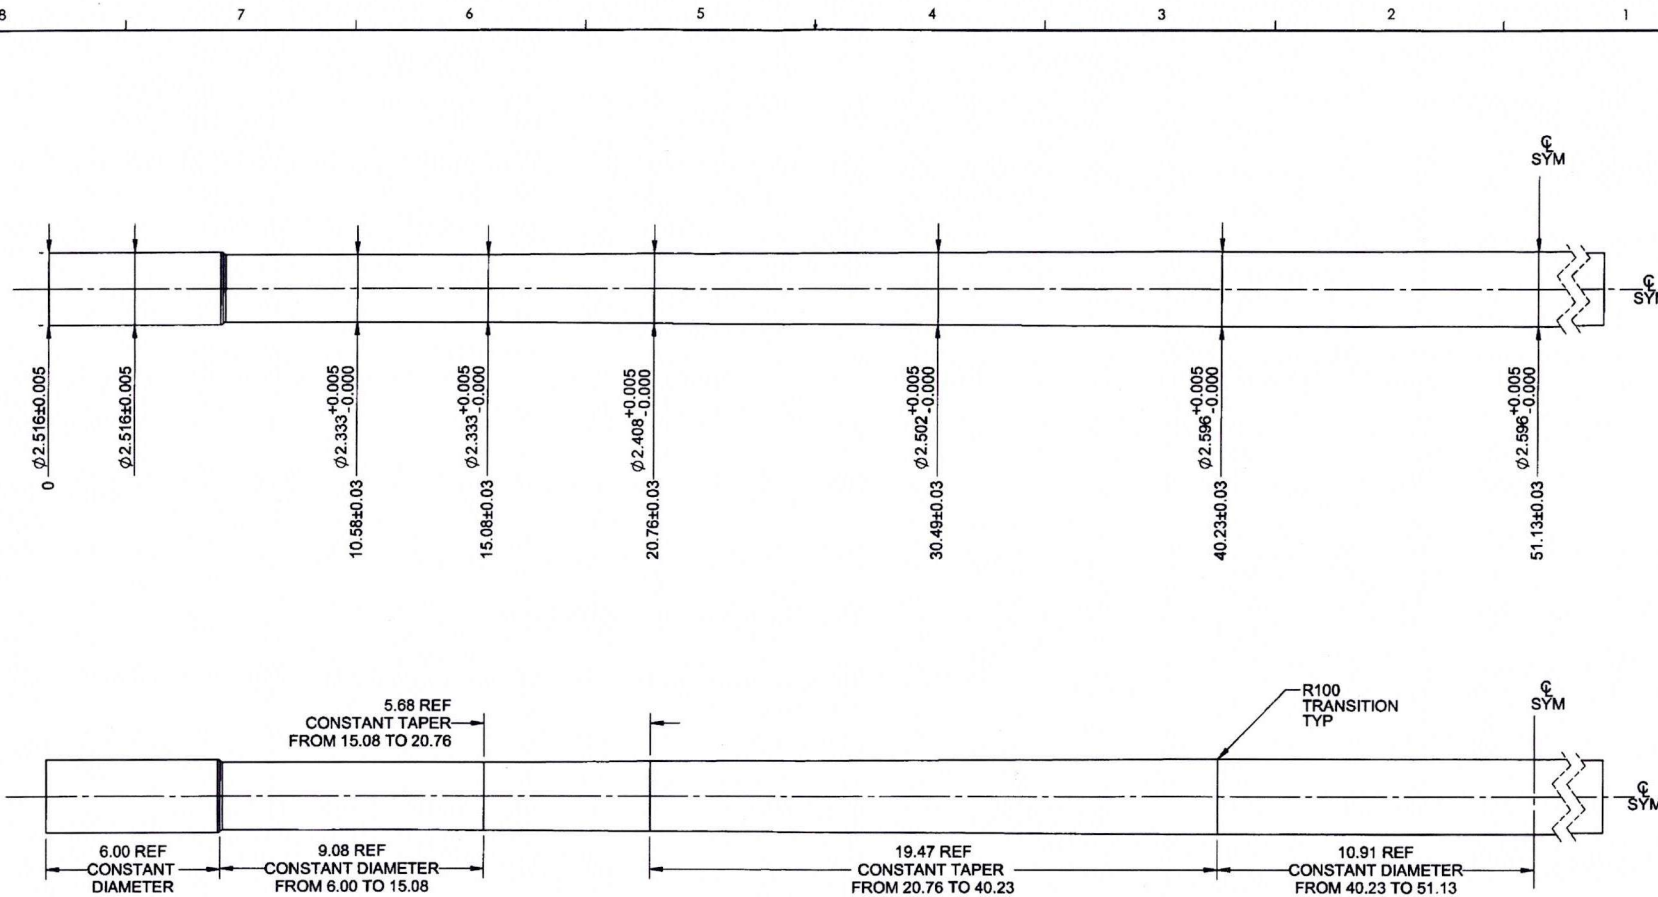

D119-796-141TRN CROSSTUBE, FWD

NOTES:

- 1) MATERIAL: MANUFACTURE FROM D6024-103 (PREFERRED) OR D6005-103
FINISHED LENGTH = 102.26 ±0.020 (BEFORE BENDING/TRIMMING)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 16.70 lbs
- 8) PART IS SYMMETRICAL ABOUT CENTERLINE

RELEASED
2015-11-04

APPROVED

DESIGN	AP	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	AJS	DRAWING NO.	REV. H
MFG. APPR.	JLM	D119-796-141	SHEET 5 OF 6
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII FWD)	NTS
DATE	15.10.13	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

Entered: _____ Date: _____




WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☒ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042)	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Presservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details:					

D119-796-141TRN CROSSTUBE, FWD
SUPPLEMENTAL VIEW: NOMINAL WALL THICKNESS



DETAIL F
SCALE 2X

CHAMFER ID
AS REQUIRED
FOR TOOLING

0.258 REF
NOMINAL WALL

0.167 REF
NOMINAL WALL
10.58±0.03

0.167 REF
NOMINAL WALL
15.08±0.03

0.204 REF
NOMINAL WALL
20.76±0.03

0.251 REF
NOMINAL WALL
30.49±0.03

0.298 REF
NOMINAL WALL
40.23±0.03

0.298 REF
NOMINAL WALL
51.13±0.03

C
SYM

C
SYM

RELEASED
2015-11-04

APPROVED

DESIGN	AP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	AJS	DRAWING NO.	REV. H
MFG. APPR.	JLM	D119-796-141	SHEET 6 OF 6
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII FWD)	NTS
DATE	15.10.13	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

Entered: _____ Date: _____



WORK ORDER NON-CONFORMANCE / ROUTE UPDATE

NCR No. _____

Route update only ☐

Job: _____ Part No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐	DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Eng. (Non-AW) ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Engineering ☐ Water Jet ☐ Supplier ☐ Quality ☐			
Date : _____	Sequence #: _____	QTY Affected : _____		MRB (QSI042)	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor	
				QC / QA Coordinator	
Root Cause Operator ☐ Manufacturing Process ☐ Equip/Tooling ☐ Handling/Presservation ☐ Material ☐ Product Improvement ☐ Process Improvement ☐ Human Factors ☐		FAULT CATEGORY ☐ Pressure/Forced ☐ Bending ☐ Crushing ☐ Cracks ☐ Crimp/Kink/Ripple/Wave/Twist ☐ Marks/Chatter ☐ Mislabeled ☐ Contamination ☐ Misaligned/off center ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Incomplete/Unclear Instructions ☐ Drill Holes ☐ Fit/Function ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain Direction ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set/Set-up ☐ Positioned Wrong ☐ Outside Tolerance ☐ Drawing ☐ Finish ☐ Part Lost/Missing ☐ Misread			
Other/Details: _____					



Dart Aerospace Ltd.
1270 Aberdeen St
Hawkesbury, ON
K6A 1K7
Canada

Tel (613) 632-5200

PURCHASE ORDER **PO042049**

Supplier: SKY002-VC
Skyservice
6120 Midfield Road
Mississauga
ON
L5P 1B1 Canada
Phone: 905-678-5636
Fax: 905-678-5841

PO No: PO042049
PO Date: 12/14/18
Due Date: 12/18/18
Purchase Order
Revision:
Revision Date:
Ship-To Contact: Phone:

Ship To: 1270 Aberdeen Street
Hawkesbury
ON
K6A 1K7 Canada
Phone: 613-632-5200

Via: Ground
Pynt Terms: Net 30
Freight Terms:
Special Comments:

Items

Line Item	Job	Part	Description	Status	Account	Due Date	Order Quantity	Received Quantity	Balance	Unit Price (CAD)	Extended Price
1	184179	D4464-041	Fuel Tank Assembly : Various STC's ISSUE P/O : LIQUID PENETRANT INSPECTION AS PER QSI 038 OR LPI AS PER ASTM 1417 LEVEL 2	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
2	187276	D119-796-141	Fwd Crosstube Installation Without Step (No Hardware) : TC STC SH14-45-Issue 1, FAA STC SR03504NY 15/01/28, EASA STC 10052022 Revision 1 15/02/13, DGCA INDIA LoA 07-09/2011-AED (Part) 15/07/16, BRAZIL STC 2015S07-16 15/07/30, CAAP PHILIPPINES LoA 16/05/11, CHINA VSTC0757 16/07/22, RUSSIA STC CT316-A119 16/08/11, DGAC INDONESIA STC SR025 18/02/19 *** WEAR LATEX GLOVES WHEN HANDLING CROSSTUBE*** Liquid Penetrant Inspection as per QSI 038Or Issue P/O: _____ LPI as per ASTM 1417 Level 2 Attach copy of NDT results to work order	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64



Dart Aerospace Ltd.
1270 Aberdeen St
Hawkesbury, ON
K6A 1K7
Canada

Tel (613) 632-5200

PURCHASE ORDER **PO042049**

Items

Line Item	Job	Part	Description	Status	Account	Due Date	Order Quantity	Received Quantity	Balance	Unit Price (CAD)	Extended Price
	187278		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
	187277		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
	187275		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
Sub Total:							4	0	4		\$514.55

DAS
38
9-89

3	185374	D212-664-101	Fwd Crosstube - High : TC STC SH01-9 Issue 3, FAA STC SR01298NY 09/01/08, EASA STC EASA.IM.R.S.01304 07/03/06, DGAC MEXICO STC IA-316/2015 15/06/17 *** WEAR LATEX GLOVES WHEN HANDLING CROSSTUBE*** Liquid Penetrant Inspection as per QSI 038 LPI as per ASTM 1417 Level 2 Attach copy of NDT results to work order	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
	186489		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
Sub Total:							2	0	2		\$257.27

4	183805	D119-796-241	Aft Crosstube Installation Without Step (No Hardware) : TC STC SH14-45-Issue 1, FAA STC SR03504NY 15/01/28, EASA STC 10052022 Revision 1 15/02/13, DGCA INDIA LoA 07-09/2011-AED (Part) 15/07/16, BRAZIL STC 2015S07-16 15/07/30, CAAP PHILIPPINES LoA 16/05/11, CHINA VSTC0757 16/07/22, RUSSIA STC CT316-A119 16/08/11, DGAC INDONESIA STC SR025 18/02/19 *** WEAR LATEX GLOVES WHEN HANDLING CROSSTUBE***	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
	187272		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
	183806		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
	187271		DEC 17 2018	Firmed	-	12/18/18	1 pcs	0 pcs	1 pcs	\$128.63636/pcs	\$128.64
Sub Total:							4	0	4		\$514.55



Dart Aerospace Ltd.
1270 Aberdeen St
Hawkesbury, ON
K6A 1K7
Canada

Tel (613) 632-5200

PURCHASE ORDER

PO042049


Items

Line Item	Job	Part	Description	Status	Account	Due Date	Order Quantity	Received Quantity	Balance	Unit Price (CAD)	Extended Price
										Grand Total:	\$1,415.00

Order Notes

Terms & Condition of Purchasing(Suppliers) and Procurement Quality Clauses are an integral part of our AS9100 requirements. To learn in detail, please visit www.dartaerospace.com for further explanation.

Plex 12/17/18 1:33 PM dart.tsimiklis.chrisoula

**skyservice****Work Order Traveler**
Sky Service F.B.O. Inc.

10105 Ryan Avenue, Dorval, Quebec, H9P 1A2

TCCA AMO 53-89 / EASA 145.7142 / BDA AMO 385

WO #: MWO38591	Customer: Dart Aerospace Ltd.	Dept: NDT YUL	Reference: PO042049
Descr:	PN:	S/N:	Qty: 1
Make:	Model:	Reg:	A/C S/N:
TSN:	CSN:	TSO:	
Task: UNSCHEDULED			Sequence: 1

Work Required:**CARRY OUT NDT ON:**

- ✓ 1 FUEL TANK ASSY , P/N# D4464-041 , J/S# 184179
- ✓ 2 FWD CROSSTUBES , P/N# D212-664-101 , J/S# 185374 , 186489
- ✓ 4 FWD CROSSTUBES , P/N D119-796-141 , J/S# 187275 , 187276 , 187277 , 187278
- ✓ 4 AFT CROSSTUBES , P/N# D119-796-241 , J/S# 183805 , 183806 , 187271 , 187272

Action Taken:						Date:	Initial/Stamp:
LPI C/O IAW ASTM E-1417M-16 NO CRACK FOUND NO LEAK FOUND PEN. ZL-56, MPO13600, CLEANER SKC-S MPO13923 , DEV. MPO11715 , UV LIGHT M-20142						DEC 14 2018	DAS 38 9-89 m DOT-APP 20 53-89
Description	Location	P/N	Qty	Batch	S/N Off	S/N On	

I certified that the maintenance described above has been performed in accordance with the applicable standard of airworthiness.

Signature:	ACA/SCA Stamp	Date:
Name: RAFIK MELIKIAN	DOT-APP 20 53-89	DEC 14 2018
